

# Project Tracking & Rollup DASHBOARD

**Project Name** EPDP: Internationalized Domain Names      **Program** gTLD      **Project Sponsor** GNSO Council

**Project Information**

**05/20/21**

Current Start


**08/18/23**

Current Finish

**28%**

% Complete

**Tasks by Status**



**Project Contacts**

**Donna Austin**

Chair

**Justine Chew**

Vice\_Chair

**Farell Folly**

Liaison


**Ariel Liang**

Staff\_Lead

**Steve Chan**

Project\_Manager

**Participant Summary**

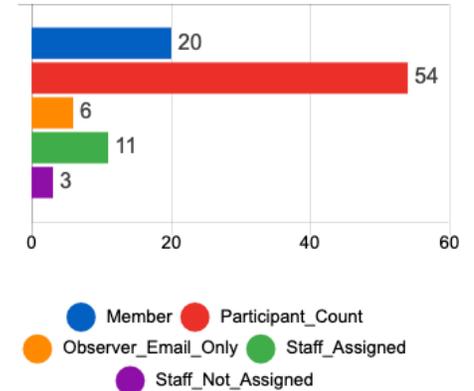

**Project Status & Health**

**Project Status:** On-Schedule

**Project Health:** On-Target

● Not\_Started ● Complete ● In\_Progress

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021			2022			2023					
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
	<b>EPDP: Internationalized Domain Names</b>	<b>05/20/21</b>	<b>08/18/23</b>	<b>28%</b>	<b>In Progress</b>	EPDP: Internationalized Domain Names											
	<b>PROJECT CONTROL</b>	<b>05/20/21</b>	<b>07/10/23</b>	<b>44%</b>	<b>In Progress</b>	PROJECT CONTROL											
	<b>GROUP DELIBERATIONS</b>	<b>08/11/21</b>	<b>03/16/23</b>	<b>25%</b>	<b>In Progress</b>	GROUP DELIBERATIONS											
●	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	08/25/21	11/02/21	61%	In Progress	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR											
●	Topic B Deliberations: "Same entity" at the top-level	11/03/21	12/28/21			Topic B Deliberations: "Same entity" at the top-level											
●	Topic C Deliberations: "Same entity" at the second-level	12/29/21	02/22/22			Topic C Deliberations: "Same entity" at the second-level											
	Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	02/23/22	05/24/22			Topic D Deliberations: Adjustments in registry agreement, registry service, registry tran...											
	Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	05/25/22	08/02/22			Topic E Deliberations: Adjustments to objection process, string similarity review, string...											
	Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	08/03/22	09/27/22			Topic F Deliberations: Adjustments in registration dispute resolution procedures											
	Topic G Deliberations: Process to update the IDN Implementation Guidelines	09/28/22	11/04/22			Topic G Deliberations: Process to update the IDN Implementation Guidelines											
	<b>INITIAL REPORT</b>	<b>09/20/21</b>	<b>02/03/23</b>	<b>16%</b>	<b>In Progress</b>	INITIAL REPORT											
	Publish Initial Report	12/16/22	12/16/22			Publish Initial Report											
	<b>FINAL REPORT</b>	<b>02/06/23</b>	<b>04/07/23</b>		<b>Not Started</b>	FINAL REPORT											
	Review of public comments	02/06/23	03/17/23			Review of public comments											
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			Submission of Final Report to the GNSO Council											

## 4 - Working Group

**Title:** EPDP - Internationalized Domain Names (EPDP\_IDN)

**Description & Scope:** On 20 May 2021, the GNSO Council passed a resolution to initiate the Expedited Policy Development Process (EPDP) on Internationalized Domain Names and adopt its charter. The EPDP Team is tasked with providing the GNSO Council with policy recommendations on: 1) the definition of gTLDs and the management of variant labels; and 2) how the IDN Implementation Guidelines, which Contracted Parties are required to comply with, should be updated in the future.

**Composition:**

<b>Chair:</b>	Donna Austin
<b>Vice Chair:</b>	Justine Chew
<b>Council Liaison:</b>	Farell Folly
<b>Staff:</b>	A. Liang, S. Chan, E. Barabas.
<b># Participants:</b>	74 Participants ( <a href="#">link</a> )
<b># Observers:</b>	9
<b>Tools:</b>	<a href="#">Mailing List</a> / <a href="#">Meeting Schedule</a> / <a href="#">Wiki</a>
<b>Charter:</b>	<a href="#">Charter</a>

**Project Management:**

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	20 May 2021	20 May 2021	245	09 Jun 2023	TBD

Program	Progress	Status	Health
gTLD	28%	<span style="color: green; font-size: 20px;">●</span>	<span style="color: green; font-size: 20px;">■</span>

**STATUS:** ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

**HEALTH:** ■ On-Target ■ At-Risk ■ In-Trouble

**Milestones/Work plan (link):**

Milestone/Task	Date	
Project Start	May-21	✓
<a href="#">Scoping Team Report</a>	Jan-20	✓
<a href="#">Charter</a> Approved	May-21	✓
EPDP Initiation <a href="#">Request Approved</a>	May-21	✓
1st Plenary meeting	Aug-21	✓
SO/AC & SG/C Input to PDP	Nov-21	✓
Project Plan and Work plan Adoption	Oct-21	✓
Issue Deliberations	Mar-23	
Populate draft report w/ findings & potential recs.	Oct-22	
Assemble initial conclusions	Oct-22	
Discuss/approve findings and interim recs.	Nov-22	
Consolidate interim recommendations and findings	Nov-22	
Issue report for public comment	Dec-22	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Apr-23	
Determine consensus levels on recommendations	Apr-23	
Adopt final recommendations and report	Apr-23	
Send final report to GNSO Council	Apr-23	
GNSO Council adoption of consensus recs.	May-23	
Issue public comment for Board consideration	Jun-23	
ICANN Board adoption of consensus recs.	Oct-23	
Prior period % Complete	25%	

**Status/Health Rationale:**

- This project was initiated on 20 May 2021 and continues with a Status of "On-Schedule" and Health of "On-Target".

**Current Activities:**

- Continue substantive deliberations on Topic A. The EPDP Team is making good progress on the ten questions contained in Topic A, with all questions having been discussed to some extent. Draft outcome language has been agreed for three out of the ten questions, and it is anticipated that draft outcome language for the remaining Topic A questions will be completed in February.

**Planned Activities:**

- Conduct an engagement session with SSAC members to discuss their early input and provide the EPDP Team an opportunity to ask SSAC members specific questions about Charter questions. The EPDP Team does not include members representing SSAC and as such this is an important engagement opportunity.
- Initiate Topics B & C deliberations.

**Open Issues, Risks & Mitigation Plan:**

- Leadership is actively reviewing the current order of Charter questions to ensure that a logical order is being followed and provide efficiencies to deliberations. Leadership also intends to revisit the project plan to assess whether the original planning assumptions were reasonable. Council will be informed if any changes are considered necessary.
- At the time the Charter was developed, it was assumed that the SubPro recommendations, particularly those relating to IDNs under Topic 25, would have been approved by the ICANN Board. The IDN EPDP is conducting its work with the expectation that the SubPro recommendations will be approved by the Board at some future date. However, it has been necessary for the EPDP Team to make assumptions about the implementation of those recommendations in order to address the Charter questions. While these assumptions are believed to be sound, the Council should be aware of the possible ripple effect or potential risk to the EPDP Team work in the event that the Board does not adopt the related SubPro recommendations.

**Completed in prior period(s):**

- Completed and distributed [Project Package](#) for December.

# Project Tracking & Rollup DASHBOARD



## Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name <b>At-Large Advisory Committee (ALAC)</b>					
TV Gopal	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Hadia Elminiawi	Participant		07/14/21		<a href="https://community.icann.org">https://community.icann.org</a>
Satish Babu	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Lianna Galstyan	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Abdulkarim Oloyede	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Justine Chew	Member	Vice-chair	05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Commercial Business Users Constituency (BC)</b>					
Mark William Datysgeld	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Expedited Policy Development Process - IDNs</b>					
Donna Austin	Member	Chair	08/10/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>GNSO Council</b>					
Ekue Farell Folly	Member	Liaison	07/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Governmental Advisory Committee (GAC)</b>					
Hamza Onoruoiza Salami	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
T. Santhosh	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Nigel Hickson	Member		07/12/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>ICANN Board</b>					
Edmon Chung	Member	Liaison	07/27/21		<a href="https://community.icann.org">https://community.icann.org</a>
Akinori Maemura	Member	Liaison	11/18/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Independent</b>					
Abdalmonem Galila	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Gao Lei	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Nabil Benamar	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Lisa Liang	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Anil Jain	Participant		07/30/21		<a href="https://community.icann.org">https://community.icann.org</a>
Quoc Pham	Participant		08/13/21		<a href="https://community.icann.org">https://community.icann.org</a>
Kenny Huang	Guest		10/26/21	10/26/21	
Group Selected / Nominated By: Group Name <b>Intellectual Property Constituency (IPC)</b>					
Brian King	Member		05/25/21	11/08/21	<a href="https://community.icann.org">https://community.icann.org</a>
Jeffrey Neuman	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>					
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Steve Chan	Staff - Assigned		05/25/21		
Emily Barabas	Staff - Assigned		05/25/21		
Terri Agnew	Staff - Assigned		05/25/21		
Sarmad Hussain	Staff - Assigned	Liaison	05/25/21		
Nathalie Peregrine	Staff - Assigned		05/25/21		
Pitinan Kooarmornpatana	Staff - Assigned		05/25/21		
Ariel Liang	Staff - Assigned		05/25/21		
Julie Bisland	Staff - Assigned		05/25/21		
Michelle DeSmyter	Staff - Assigned		08/18/21		
Devan Reed	Staff - Assigned		12/02/21		
Group Selected / Nominated By: Group Name <b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>					
Christian Dawson	Participant		07/12/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Non-Commercial Stakeholder Group (NCSG)</b>					
Tomslin Samme-Nlar	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Akinremi Peter Taiwo	Member		07/15/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Registrar Stakeholder Group (RrSG)</b>					
Michael Bauland	Member		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>
Duwei Chen	Member		09/26/21		<a href="https://community.icann.org">https://community.icann.org</a>
Group Selected / Nominated By: Group Name <b>Registry Stakeholder Group (RySG)</b>					
Jennifer Chuna	Participant		05/25/21		<a href="https://community.icann.org">https://community.icann.org</a>


Jerry Sen	Participant	05/25/21	<a href="https://community.icann.org">https://community.icann.org</a>
Wei (Wesley) Wang	Participant	07/13/21	<a href="https://community.icann.org">https://community.icann.org</a>
Maxim Alzoba	Member	05/25/21	<a href="https://community.icann.org">https://community.icann.org</a>
Joseph Chiu-Kit Yee	Member	07/06/21	<a href="https://community.icann.org">https://community.icann.org</a>
Dennis Tan Tanaka	Member	05/25/21	<a href="https://community.icann.org">https://community.icann.org</a>

# Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics



Mailman Activity

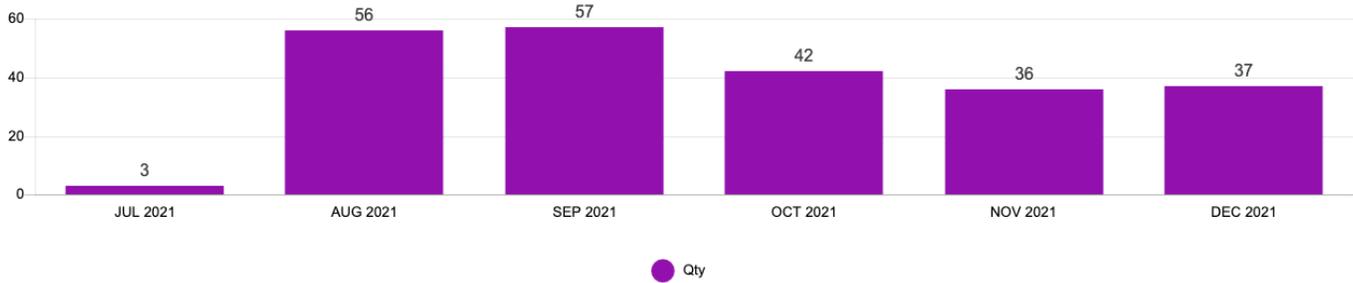

Meeting Activity

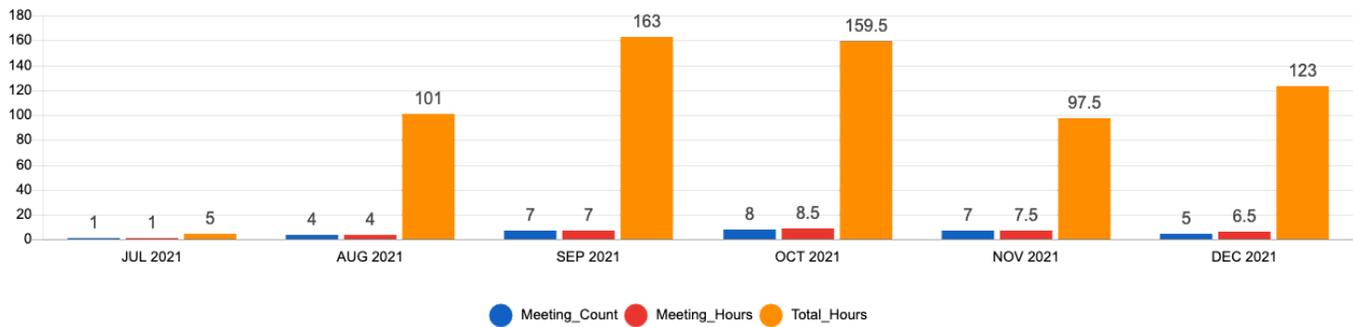

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
<b>Total</b>	Sum <b>518</b>	Sum <b>366</b>	Avg <b>70.7%</b>
Primary <b>At-Large Advisory Committee (ALAC)</b>	Sum <b>100</b>	Sum <b>81</b>	Avg <b>81.0%</b>
Attendee Name <b>Abdulkarim Oloyede</b>	Sum <b>17</b>	Sum <b>15</b>	Avg <b>88.2%</b>
Attendee Name <b>Hadia Elminiawi</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Attendee Name <b>Justine Chew</b>	Sum <b>17</b>	Sum <b>17</b>	Avg <b>100.0%</b>
Attendee Name <b>Lianna Galstyan</b>	Sum <b>17</b>	Sum <b>12</b>	Avg <b>70.6%</b>
Attendee Name <b>Satish Babu</b>	Sum <b>17</b>	Sum <b>15</b>	Avg <b>88.2%</b>
Attendee Name <b>TV Gopal</b>	Sum <b>15</b>	Sum <b>6</b>	Avg <b>40.0%</b>
Primary <b>Commercial Business Users Constituency (BC)</b>	Sum <b>17</b>	Sum <b>2</b>	Avg <b>11.8%</b>
Attendee Name <b>Mark William Datysgeld</b>	Sum <b>17</b>	Sum <b>2</b>	Avg <b>11.8%</b>

Primary <b>Expedited Policy Development Process - IDNs</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Attendee Name <b>Donna Austin</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Primary <b>GNSO Council</b>	Sum <b>17</b>	Sum <b>14</b>	Avg <b>82.4%</b>
Attendee Name <b>Ekue Farell Folly</b>	Sum <b>17</b>	Sum <b>14</b>	Avg <b>82.4%</b>
Primary <b>Governmental Advisory Committee (GAC)</b>	Sum <b>50</b>	Sum <b>38</b>	Avg <b>76.0%</b>
Attendee Name <b>Hamza Onoruoza Salami</b>	Sum <b>16</b>	Sum <b>12</b>	Avg <b>75.0%</b>
Attendee Name <b>Nigel Hickson</b>	Sum <b>17</b>	Sum <b>13</b>	Avg <b>76.5%</b>
Attendee Name <b>T. Santhosh</b>	Sum <b>17</b>	Sum <b>13</b>	Avg <b>76.5%</b>
Primary <b>ICANN Board</b>	Sum <b>20</b>	Sum <b>19</b>	Avg <b>95.0%</b>
Attendee Name <b>Akinori Maemura</b>	Sum <b>3</b>	Sum <b>3</b>	Avg <b>100.0%</b>
Attendee Name <b>Edmon Chung</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Primary <b>Independent</b>	Sum <b>92</b>	Sum <b>45</b>	Avg <b>48.9%</b>
Attendee Name <b>Abdalmonem Galila</b>	Sum <b>15</b>	Sum <b>2</b>	Avg <b>13.3%</b>
Attendee Name <b>ANIL JAIN</b>	Sum <b>17</b>	Sum <b>15</b>	Avg <b>88.2%</b>
Attendee Name <b>Gao Lei</b>	Sum <b>14</b>	Sum <b>1</b>	Avg <b>7.1%</b>
Attendee Name <b>Kenny Huang</b>	Sum <b>1</b>	Sum <b>1</b>	Avg <b>100.0%</b>
Attendee Name <b>Lisa Liang</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Attendee Name <b>Nabil Benamar</b>	Sum <b>14</b>	Sum <b>0</b>	Avg <b>0.0%</b>
Attendee Name <b>Quoc Pham</b>	Sum <b>14</b>	Sum <b>10</b>	Avg <b>71.4%</b>
Primary <b>Intellectual Property Constituency (IPC)</b>	Sum <b>30</b>	Sum <b>23</b>	Avg <b>76.7%</b>
Attendee Name <b>Brian King</b>	Sum <b>13</b>	Sum <b>10</b>	Avg <b>76.9%</b>
Attendee Name <b>Jeffrey Neuman</b>	Sum <b>17</b>	Sum <b>13</b>	Avg <b>76.5%</b>
Primary <b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	Sum <b>15</b>	Sum <b>9</b>	Avg <b>60.0%</b>
Attendee Name <b>Christian Dawson</b>	Sum <b>15</b>	Sum <b>9</b>	Avg <b>60.0%</b>
Primary <b>Non-Commercial Stakeholder Group (NCSG)</b>	Sum <b>34</b>	Sum <b>15</b>	Avg <b>44.1%</b>
Attendee Name <b>Akinremi Peter Taiwo</b>	Sum <b>17</b>	Sum <b>7</b>	Avg <b>41.2%</b>
Attendee Name <b>Tomslin Samme-Nlar</b>	Sum <b>17</b>	Sum <b>8</b>	Avg <b>47.1%</b>
Primary <b>Registrar Stakeholder Group (RrSG)</b>	Sum <b>27</b>	Sum <b>23</b>	Avg <b>85.2%</b>
Attendee Name <b>Duowei Chen</b>	Sum <b>10</b>	Sum <b>8</b>	Avg <b>80.0%</b>
Attendee Name <b>Michael Bauland</b>	Sum <b>17</b>	Sum <b>15</b>	Avg <b>88.2%</b>
Primary <b>Registry Stakeholder Group (RySG)</b>	Sum <b>99</b>	Sum <b>81</b>	Avg <b>81.8%</b>
Attendee Name <b>Dennis Tan Tanaka</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Attendee Name <b>Jennifer Chung</b>	Sum <b>16</b>	Sum <b>14</b>	Avg <b>87.5%</b>
Attendee Name <b>Jerry Sen</b>	Sum <b>17</b>	Sum <b>17</b>	Avg <b>100.0%</b>
Attendee Name <b>Joseph Chiu-Kit Yee</b>	Sum <b>17</b>	Sum <b>16</b>	Avg <b>94.1%</b>
Attendee Name <b>Maxim Alzoba</b>	Sum <b>17</b>	Sum <b>15</b>	Avg <b>88.2%</b>
Attendee Name <b>Wei (Wesley) Wang</b>	Sum <b>15</b>	Sum <b>3</b>	Avg <b>20.0%</b>

Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Q1					Q2					Q3					Q4														
							Q1					Q2					Q3					Q4														
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
1 EPDP: Internationalized Domain Names	587d	05/20/21	08/18/23		28%	In Progress	[Gantt bar spanning from May 2021 to August 2023]																													
2 PROJECT CONTROL	558d	05/20/21	07/10/23		44%	In Progress	[Gantt bar spanning from May 2021 to July 2023]																													
3 Project start confirmed	0	05/20/21	05/20/21		100%	Complete	[Gantt bar at 05/20/21]																													
4 Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	[Gantt bar at 05/20/21]																													
5 Confirmation of Team	60d	05/20/21	08/11/21	3	100%	Complete	[Gantt bar from 05/20/21 to 08/11/21]																													
6 Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	[Gantt bar from 05/20/21 to 07/22/21]																													
7 Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	[Gantt bar from 05/20/21 to 07/22/21]																													
8 Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	[Gantt bar from 07/23/21 to 08/10/21]																													
9 Project Management	512d	07/23/21	07/10/23		26%	In Progress	[Gantt bar spanning from July 2021 to July 2023]																													
10 Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	[Gantt bar from 07/23/21 to 09/30/21]																													
11 Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	[Gantt bar from 10/01/21 to 10/28/21]																													
12 Develop monthly Project Packages and deliver to Group & Council	370d	10/29/21	03/30/23	11	12%	In Progress	[Gantt bar spanning from October 2021 to March 2023]																													
13 Leadership Sub team	440d	07/23/21	03/30/23		26%	In Progress	[Gantt bar spanning from July 2021 to March 2023]																													
14 On-going preparation and planning of group activities	440d	07/23/21	03/30/23	6	26%	In Progress	[Gantt bar spanning from July 2021 to March 2023]																													
15 Close project and transition project to implementation	1d	07/10/23	07/10/23	14, 165	0%		[Gantt bar at 07/10/23]																													
16 GROUP DELIBERATIONS	417d	08/11/21	03/16/23		25%	In Progress	[Gantt bar spanning from August 2021 to March 2023]																													
17 First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	[Gantt bar at 08/11/21]																													
18 Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	[Gantt bar from 08/11/21 to 08/24/21]																													
19 Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	[Gantt bar from 08/11/21 to 08/24/21]																													
20 Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	[Gantt bar from 08/11/21 to 09/17/21]																													
21 Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	[Gantt bar from 09/09/21 to 11/29/21]																													
26 Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	50d	08/25/21	11/02/21		61%	In Progress	[Gantt bar from 08/25/21 to 11/02/21]																													
44 Topic B Deliberations: "Same entity" at the top-level	40d	11/03/21	12/28/21				[Gantt bar from 11/03/21 to 12/28/21]																													
57 Topic C Deliberations: "Same entity" at the second-level	40d	12/29/21	02/22/22				[Gantt bar from 12/29/21 to 02/22/22]																													
71 Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	65d	02/23/22	05/24/22				[Gantt bar from 02/23/22 to 05/24/22]																													
87 Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	50d	05/25/22	08/02/22				[Gantt bar from 05/25/22 to 08/02/22]																													
102 Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	40d	08/03/22	09/27/22				[Gantt bar from 08/03/22 to 09/27/22]																													
112 Topic G Deliberations: Process to update the IDN Implementation Guidelines	28d	09/28/22	11/04/22				[Gantt bar from 09/28/22 to 11/04/22]																													
121 Unplanned Issues & Tasks	0	08/24/21	08/24/21				[Gantt bar at 08/24/21]																													
138 Key Group Events	364d	10/25/21	03/16/23		17%	In Progress	[Gantt bar spanning from October 2021 to March 2023]																													
145 INITIAL REPORT	360d	09/20/21	02/03/23		16%	In Progress	[Gantt bar spanning from September 2021 to February 2023]																													
146 Populate stable drafts as required	300d	09/20/21	11/11/22	20	20%	In Progress	[Gantt bar from 09/20/21 to 11/11/22]																													
147 Discuss/approve findings and interim recommendations	10d	11/14/22	11/25/22	146			[Gantt bar from 11/14/22 to 11/25/22]																													
148 Consolidate interim recommendations and findings	10d	11/28/22	12/09/22	147			[Gantt bar from 11/28/22 to 12/09/22]																													
149 Build Draft Report for public comment	10d	11/28/22	12/09/22	147			[Gantt bar from 11/28/22 to 12/09/22]																													
150 Approve Draft Report for public comment	5d	12/12/22	12/16/22	149			[Gantt bar from 12/12/22 to 12/16/22]																													
151 Publish Initial Report	0	12/16/22	12/16/22	150			[Gantt bar at 12/16/22]																													
152 Communicate Initial Report	5d	12/19/22	12/23/22	150			[Gantt bar from 12/19/22 to 12/23/22]																													
153 Public comment forum on the Initial Report (40 days)	35d	12/19/22	02/03/23	150			[Gantt bar from 12/19/22 to 02/03/23]																													
154 FINAL REPORT	45d	02/06/23	04/07/23			Not Started	[Gantt bar from 02/06/23 to 04/07/23]																													
155 Review of public comments	30d	02/06/23	03/17/23	153			[Gantt bar from 02/06/23 to 03/17/23]																													
156 Continue deliberations of policy topics towards a Final Report	30d	02/06/23	03/17/23	153			[Gantt bar from 02/06/23 to 03/17/23]																													
157 Build Final Report & Final Deliberations	5d	03/20/23	03/24/23	156			[Gantt bar from 03/20/23 to 03/24/23]																													
158 Determine consensus levels on interim recommendations	10d	03/27/23	04/07/23	157			[Gantt bar from 03/27/23 to 04/07/23]																													
159 Adopt final recommendations and report	10d	03/27/23	04/07/23	157			[Gantt bar from 03/27/23 to 04/07/23]																													
160 Submission of Final Report to the GNSO Council	0	04/07/23	04/07/23	159			[Gantt bar at 04/07/23]																													
161 POST GROUP TASKS	95d	04/10/23	08/18/23			Not Started	[Gantt bar from 04/10/23 to 08/18/23]																													
166 PDP CHECKLIST	99d	01/01/21	05/20/21				[Gantt bar from 01/01/21 to 05/20/21]																													

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #14 Report on SO/AC Early Input; Topic A/Question A4 Analysis; Topic A/Question A5 Introduction	↓	EPDP_IDN	12/02/21	12/02/21	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	12/06/21	12/06/21	Complete	
	AI	Action Item #2: Staff to draft placeholder response to charter question a4 based on the analysis conducted. WG will return to close the question once it has deliberated on charter question b4	—	Ariel Liang	12/09/21	12/03/21	Complete	
	AI	Action Item #1: WG to review draft response to charter questions and provide input by Monday 13 December 2021	—	EPDP_IDN	12/13/21	12/13/21	Complete	
	AI	<b>Action Item #3: Leadership team to see if there are additional background materials that can be leveraged to inform discussion on charter question A5</b>	—	EPDP_IDN Leadership	01/13/22			
	WP	Meeting #15 Topic A/Questions A6 & A7 Discussion	↓	EPDP_IDN	12/09/21	12/09/21	Complete	
	WP	Meeting #16 Revisit draft outcome language for Topic A/Questions A1-A3; Topic A/Questions A9 & A10 Discussion	↓	EPDP_IDN	12/17/21	12/17/21	Complete	
	AI	Action Item #1: EPDP Team members to review proposed alternative phrasing for 1.2 and indicate prior to the next meeting whether there are any concerns.	—	EPDP_IDN	12/17/21	12/17/21	Complete	
	WP	Meeting #18 TBD	—	EPDP_IDN	01/06/22			
	MS	Submit project package to GNSO Council	!	Ariel Liang	01/07/22			
	WP	Meeting #19 TBD	—	EPDP_IDN	01/13/22			
	WP	Meeting #20 TBD	—	EPDP_IDN	01/20/22			
	WP	Meeting #21 TBD	—	EPDP_IDN	01/27/22			
	WP	Meeting #22 TBD	—	EPDP_IDN	02/03/22			
	MS	Submit project package to GNSO Council	!	Ariel Liang	02/04/22			
	WP	Meeting #23 TBD	—	EPDP_IDN	02/10/22			
	WP	Meeting #24 TBD	—	EPDP_IDN	02/17/22			
	WP	Meeting #25 TBD	—	EPDP_IDN	02/24/22			
	WP	Meeting #26 TBD	—	EPDP_IDN	03/03/22			
	MS	Submit project package to GNSO Council	!	Ariel Liang	03/04/22			
	WP	Meeting ICANN73 TBD	—	EPDP_IDN	03/08/22			
